

Baton Rouge SSO Program

Progress Report



March 2011



Prepared for
City of Baton Rouge/
East Baton Rouge Parish
Department of Public Works

Prepared by
CH2MHILL
In association with
SIGMA Consulting Group, Inc.
ILSI Engineering

BATON ROUGE 
Program

Program Management



SSO Program Overview


- \$1.3B Infrastructure Improvement Program

Program Highlights


- 78 Active Projects
 - » 14 Projects Completed
 - » 28 Projects Under Construction
 - » 36 Projects in Design

During the 1st quarter of 2011, the SSO Program has continued to advance in the implementation of the Program projects. Fourteen projects have been operationally completed that include upgrading 23 pump stations, replacing or rehabilitating 2,005 manholes, and improving 424,426 linear feet (or approximately 80 miles) of gravity and forcemain pipelines in East Baton Rouge Parish.

While continuing to implement technical aspects of the Program, SSO Program staff also attended several community meetings in March to discuss Program projects. Program leadership staff participated in gatherings in Metro Council Districts 4 and 10 and discussed capacity and rehabilitation projects in their communities.

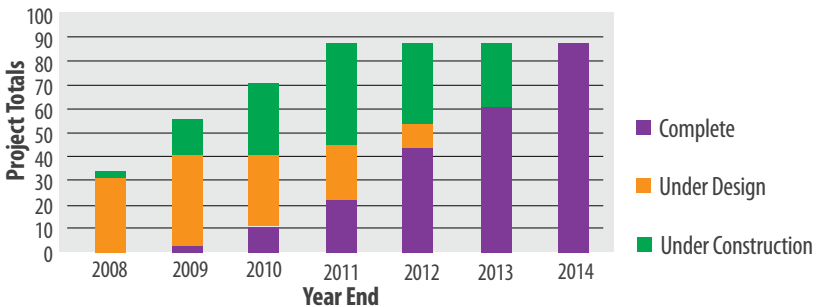

Significant construction progress of SSO Program projects will occur from 2011 until 2014.



In the Spotlight...

Thank You for Your Patience During Construction

The Program Management Team together with the Office of the Mayor-President and Department of Public Works are taking measures to minimize construction impacts to the public. We appreciate your patience and understanding during construction of these vital sewer system improvements.



- ✓ Capacity improvement and rehabilitation projects often require lane and street closures. Please pay close attention to any traffic signs or directions given by flagmen. We appreciate your patience while we are working in your area.
- ✓ We may be required to access sewer lines under sidewalks and driveways, in yards, in the public right-of-way, or in adjacent servitudes. Once construction has been completed, all sidewalks, driveways, streets, and plantings will be restored.
- ✓ We may also be required to trim tree limbs within ROWs and servitudes to bring large equipment into the work area. All trimming is performed in consultation with an arborist.
- ✓ If a public right-of-way is located on your property, a contractor will let you know. We will never ask to enter your home.
- ✓ If you have pets in your yard, please confine them while crews are working in your area.
- ✓ For your safety, always avoid construction and excavation areas.




Keeping You Informed
During Construction is
Important to Us

Call **225.588.5678**
with any
construction-related questions

Committed to Keeping You Informed

The Baton Rouge SSO Program Team is committed to keeping you informed about project activities and construction impacts that may affect residents and businesses. If you have any questions or concerns, or need more information, please contact the SSO Program Public Information Officer at 225-588-5678.

Projects Under Construction

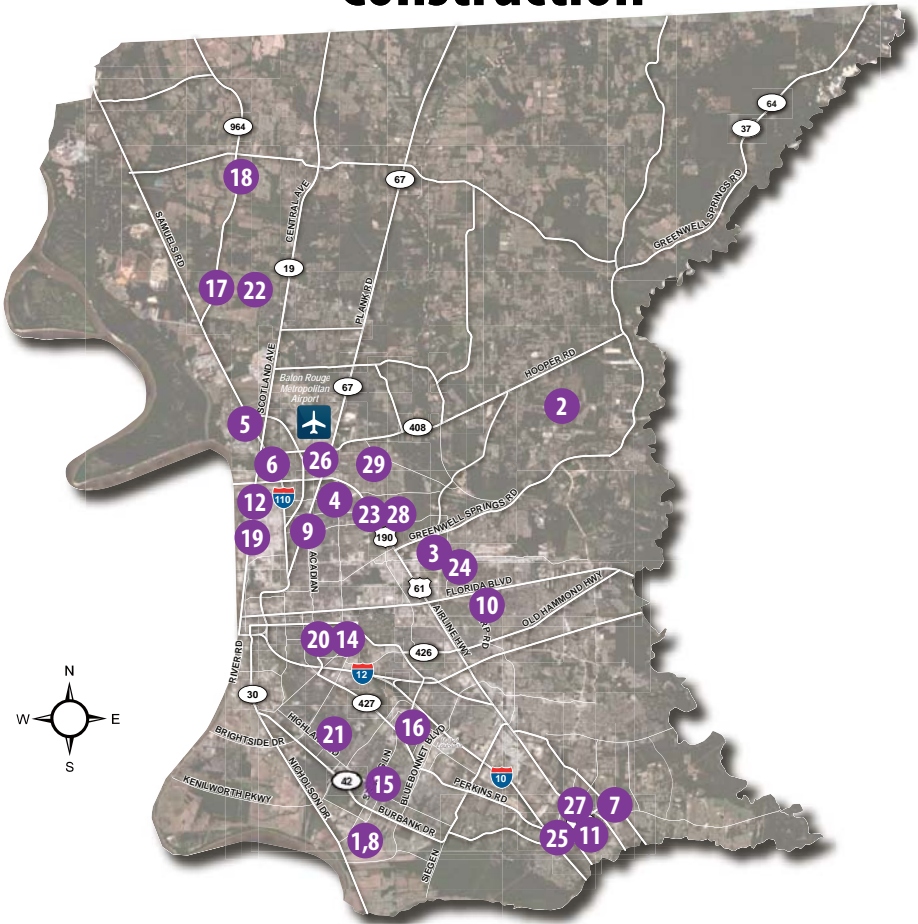

- | | | |
|--|--|--|
| <ul style="list-style-type: none"> 1 SWWTP IAPs Combined 2 Sullivan Rd/Lovett Rd/Wax Rd 3 Oak Villa Blvd – Choctaw Street 4 Comite Drive – Foster Road (Phase 2) 5 Scotland Avenue – Progress Road 6 Elm Grove Garden Road – Harding Blvd 7 Group Project 2 – Small Pump Stations 8 SWWTP Wet Weather Improve (Phase 1) 9 South Blvd-St. Joseph St/25th St – N. Acadian Thruway 10 Sharp Road – Florida Blvd | <ul style="list-style-type: none"> 11 Highland Road – Buchanan St 12 Capitol Lake Dr – Gayosa St/ 25th St – N. Acadian Thruway 13 Emergency Generators Purchasing & Installation* 14 Foster Drive – Government Street (Phase A) 15 Staring Lane FM (PH2 – Highland to Perkins) 16 Citilplace/Essen Area 17 Zachary Area Transmission Network (Phase 1) 18 Zachary Area Transmission Network (Phase 4) 19 Downtown Area –PS15, PS19, PSS9, PS60 20 Foster Drive – Government St (Phase B) | <ul style="list-style-type: none"> 21 Kenilworth Blvd – Boone Drive 22 Zachary Area Transmission Network (Phase 3) 23 Brookstown Road – Evangeline Street (Phase 1) 24 Choctaw Storage and PS Facility 25 Highland Road – Burbank Drive 26 Group Project 1A (Veterans Parkway – Gravity Mains) 27 Nicholson Dr – Highland Rd – Perkins Rd (Phase A) 28 Brookstown Road – Evangeline Street (Phase 2) 29 Silverleaf Road – Ford Street <p>* Throughout the City – Parish</p> |
|--|--|--|



1) SWWTP IAPs Combined: These Immediate Action Projects located at the South WWTP involve replacing the primary clarifier, modifying the trickling pump station, and piping/pumping modifications to the digester complex.

2) Sullivan Rd/Lovett Rd/Wax Rd: This capacity improvement project involves replacing three pump stations and upsizing approximately 4,200 linear feet of forcemain and 2,100 linear feet of gravity main.

3) Oak Villa Blvd – Choctaw Street: This rehabilitation project involves inspecting and rehabilitating, as needed, approximately 245,000 linear feet of forcemain and 990 manholes.



4) Comite Drive – Foster Road (Phase 2): Phase 2 of this capacity project involves upgrading approximately 1,361 linear feet of gravity main.

5) Scotland Avenue – Progress Road: This rehabilitation project involves inspecting and rehabilitating, as needed, approximately 208,000 linear feet of forcemain and 300 manholes.

6) Elm Grove Garden Road – Harding Blvd: This rehabilitation project involves rehabilitating approximately 199,500 linear feet of gravity main and 839 manholes.



7) Group Project 2 – Small Pump Stations: This capacity improvement project involves replacing seven pump stations that will work in conjunction with the forcemain upgrades in other South Forced Lower Basin projects.

8) SWWTP Wet Weather Improvements (Phase 1): Phase 1 will provide wet weather storage, influent pumping, and preliminary treatment at the South WWTP.

9) South Blvd-St. Joseph St/25th St – N. Acadian Thruway: This capacity improvement project involves upgrading approximately 18,360 linear feet of forcemain and 3,000 linear feet of gravity main.

10) Sharp Road – Florida Blvd: This rehabilitation project involves rehabilitating approximately 274,475 linear feet of gravity main and 1,154 manholes.

11) Highland Road – Buchanan Street: This capacity improvement project involves upgrading approximately 4,465 linear feet of forcemain and 8,390 linear feet of gravity main.

12) Capitol Lake Dr – Gayosa St/25th St – N. Acadian Thruway: This capacity improvement project involves upgrading approximately 19,320 linear feet of forcemain and 19,150 linear feet of gravity main.

13) Emergency Generators Purchasing and Installation: This project involves purchasing and installing generators at each of the pump stations in East Baton Rouge Parish to ensure continuity of service during power failures.

14) Foster Drive – Government Street (Phase A): This rehabilitation project involves replacing and rehabilitating 629 manholes and improvements to 80,600 linear feet of gravity main.

15) Staring Lane FM (PH2 – Highland to Perkins): This capacity project involves upgrading approximately 12,363 linear feet of forcemain.

16) Citiplace/Essen Area – PS119 and FM Improvements: This capacity project involves replacing one pump station and upgrading approximately 8,100 linear feet of forcemain.

17) Zachary Area Transmission Network (Phase 1): Phase 1 will involve upgrading three pump stations.

18) Zachary Area Transmission Network (Phase 4): Phase 4 of this capacity project will upgrade approximately 42,500 linear feet of forcemain.

19) Downtown Area –PS15, PS19, PS59, PS60: This capacity project involves upgrading three pump stations.



**20) Foster Drive – Government Street (Phase B):**

This rehabilitation project involves upgrading approximately 78,700 linear feet of gravity main.

21) Kenilworth Blvd – Boone Drive: This rehabilitation project involves rehabilitating approximately 72,000 linear feet of gravity main and 1,159 manholes.

22) Zachary Area Transmission Network (Phase 3):

Phase 3 of this capacity project will improve approximately 27,000 linear feet of forcemain.

23) Brookstown Road – Evangeline Street (Phase 1):

This rehabilitation project involves rehabilitating approximately 161,000 linear feet of gravity main and 1,150 manholes.



24) Choctaw Storage and PS Facility: This WWTP project involves replacing three pump stations and implementing improvements to approximately 25,000 linear feet of forcemain.

25) Highland Road – Burbank Drive: This capacity project involves upgrading approximately 39,400 linear feet of forcemain.

26) Group Project 1A (Veterans Parkway – Gravity Mains): This capacity project involves upgrading approximately 46,000 linear feet of gravity main.

27) Nicholson Dr – Highland Rd – Perkins Rd (Phase A):

This capacity project involves upgrades to approximately 8,400 linear feet of forcemain, 3,400 linear feet of gravity main and the rehabilitation/replacement of 20 manholes.

28) Brookstown Road – Evangeline Street (Phase 2):

Phase 2 of this rehabilitation project involves rehabilitating approximately 84,000 linear feet of gravity main and 1,075 manholes.

29) Silverleaf Road – Ford Street: This rehabilitation project involves implementing upgrades to 115,200 linear feet of gravity main.



Project Information

Project Components

Consultant/Contractor Information

Cost

Schedule

#	Project Name	Project Type	DPW Project #	Project Components				Consultant/Contractor Information		Construction Contract Amount	Project Start	Advertise for Construction Bid	Project End
				Number of Upgraded Pump Stations	Number of Replaced/Rehabilitated Manholes*	Linear Feet of Forcemain Improvements	Linear Feet of Gravity Main Improvements	Design Consultant	Construction Contractor				
1	Jefferson Highway-Hoo Shoo Too Road	Rehab	07-AR-US-0049	-	553	-	-	DPW	Allen & LeBlanc	\$1,769,438	5/16/2007	6/27/2008	9/22/2009
2	Staring Lane - Boone Drive	Rehab	08-AR-UF-0004	-	665	-	139,050	CSRS, Inc.	Grady Crawford	\$5,416,540	11/27/2007	1/23/2009	5/3/2010
3	Staring Lane FM (PH1 - Burbank to Highland)	Capacity	06-WC-CP-0036	-	-	2,260	-	Monroe & Corie	James Construction	\$4,615,500	1/11/2008	9/19/2008	7/2/2010
4	Gurney Road - Joor Road	Capacity	07-PS-BD-0017	1	-	14,475	-	Neel-Schaffer	Grady Crawford	\$1,543,733	1/18/2008	8/29/2008	10/15/2009
5	RMAP1 - Kleinpeter Area Upgrades	RMAP1	03-RMP-S14	1	-	2,000	-	Monroe & Corie	Allen & LeBlanc	\$324,024	2/1/2008	7/14/2008	5/8/2009
6	RMAP1 - PS136 Area Upgrades	RMAP1	99-RMP-S16	9	-	27,700	20,700	Sigma Consulting	Nottingham Construction	\$8,994,709	2/1/2008	10/26/2008	9/15/2010
7	Comite Drive - Foster Road (PH1)	Capacity	07-PS-BD-0019	3	-	12,080	-	Monroe & Corie	Hemphill Construction	\$1,923,521	3/3/2008	1/16/2009	6/30/2010
8	25th Street - North Acadian Thruway	Capacity	09-GS-UF-0008	-	-	-	-	Hartman Engineering	(design only)	-	2/2/2009	-	3/4/2010
9	NWWTP Odor Control	WWTP	07-WP-TP-0030	-	-	-	-	Environmental Eng Svcs	SEMS, Inc.	\$3,513,463	6/29/2007	10/30/2009	11/19/2010
10	Foster Road - Hooper Road	Capacity	07-FM-BD-0046	-	-	26,200	-	PEC	Hemphill Construction	\$8,761,675	2/14/2008	1/9/2009	11/30/2010
11	Burbank Road - Gardere Lane	Rehab	08-AR-UF-0003	-	787	-	168,300	CSRS, Inc.	Allen & LeBlanc	\$6,126,532	5/16/2007	11/14/2008	1/3/2011
12	RMAP1 - Industriplex Area Upgrades	RMAP1	99-RMP-S08	6	-	4,000	-	Forte & Tablada	BRH Garver	\$10,018,093	3/10/2008	10/31/2008	1/31/2011
13	Comite Drive - Foster Road (PH2)	Capacity	02-CS-HC-0001	-	-	-	1,361	Monroe & Corie	JB James Construction	\$895,957	6/23/2008	6/27/2009	2/25/2011
14	Sullivan Rd/Lovett Rd/Wax Rd	Capacity	07-PS-BD-0018	3	-	4,200	2,100	Hartman Engineering	Don M. Barron Contractor	\$2,158,346	1/17/2008	1/16/2009	4/1/2011
				23	2,005	92,915	331,511			\$56,061,532			
#	Project Name	Project Type	DPW Project #	Number of Upgraded Pump Stations	Number of Replaced/Rehabilitated Manholes*	Linear Feet of Forcemain Improvements	Linear Feet of Gravity Main Improvements	Design Consultant	Construction Contractor	Construction Contract Amount	Project Start	Advertise for Construction Bid	Project End
1	SWWTP IAPs Combined	WWTP	08-TP-BD-0031	-	-	-	-	CDM, MWH, URS Corp.	Brasfield & Gorrie	\$27,159,964	11/6/2006	12/12/2008	3/2/2011
2	Scotland Avenue - Progress Road	Rehab	09-AR-BD-0011	-	300	-	208,000	CSRS, Inc.	Magnolia Construction	\$9,207,594	9/9/2008	9/25/2009	3/14/2011
3	Oak Villa Blvd - Choctaw Street	Rehab	08-AR-UF-0005	-	990	245,000	-	CSRS, Inc.	Grady Crawford	\$8,997,369	4/14/2008	5/15/2009	6/7/2011
4	Elm Grove Garden Road - Harding Blvd	Rehab	09-AR-BD-0012	-	839	-	199,500	CSRS, Inc.	Allen & LeBlanc	\$12,989,271	10/1/2008	9/25/2009	6/13/2011
5	Emergency Generators Purchasing	Other	09-PS-BD-0037	-	-	-	-	N/A	ARCCO	\$19,100,000	2009	6/18/2010	6/30/2011
6	Group Project 2 - Small Pump Stations	Capacity	08-PS-IF-0046	7	-	-	-	ABMB Eng.	Grady Crawford	\$3,476,003	3/10/2008	3/26/2010	8/15/2011
7	Nicholson Dr - Highland Rd - Perkins Rd (PHA)	Capacity	09-FM-MS-0047A	-	20	8,400	3,400	Buchart - Horn	Grady Crawford	\$2,591,613	6/29/2009	10/29/2010	9/27/2011
8	Highland Road - Buchanan Street	Capacity	08-GS-ST-0021	-	-	4,465	8,390	Burk-Kleinpeter/Justice & Huang (JV)	Gilmore & Sons Construction	\$4,325,851	3/14/2008	4/23/2010	10/5/2011
9	Foster Drive - Government Street (PHA)	Rehab	09-AR-BD-0015A	-	629	-	80,600	CSRS, Inc.	Grady Crawford	\$4,819,752	5/25/2009	6/25/2010	10/20/2011
10	South Blvd-St. Joseph St / 25th St - N. Acadian Thrw	Capacity	08-GS-ST-0018	-	-	18,360	3,000	Evans-Graves	Reynolds, Inc.	\$17,965,049	3/27/2008	4/16/2010	1/11/2012
11	Citilace/Essex Area - PS119 and FM Improvements	Capacity	08-FM-UF-0024	1	-	8,100	-	GSA Consulting Engineers, Inc.	BRH Garver	\$2,801,502	2/25/2008	8/20/2010	2/2/2012
12	Foster Drive - Government Street (PHB)	Rehab	09-AR-BD-0015B	-	-	-	78,700	CSRS, Inc.	Insituform Technologies	\$2,863,100	5/25/2009	9/17/2010	2/17/2012
13	Capitol Lake Dr - Gayosa St / 25th St - N. Acadian Thrw	Capacity	07-PS-BD-0048	-	-	19,320	19,150	Shread-Kuykendall & Associates, Inc.	Morgan Contracting, Inc. of FL	\$10,497,568	1/14/2008	6/18/2010	2/17/2012
14	Downtown Area - PS15, PS19, PS59, PS60	Capacity	08-PS-ST-0056/57	3	-	-	-	Shaw Environmental & Infrastructure, Inc.	Guy Hopkins Construction Co.	\$4,841,000	3/24/2008	9/3/2010	2/24/2012
15	Kenilworth Blvd - Boone Drive	Rehab	09-AR-BD-0014	-	1,159	-	72,000	CSRS, Inc.	Allen & LeBlanc	\$5,168,129	3/26/2009	10/8/2010	3/16/2012
16	Silverleaf Road - Ford Street	Rehab	10-AR-BD-0041	-	-	-	115,200	CSRS, Inc.	John Plott Company	\$8,024,945	10/26/2009	1/28/2011	5/25/2012
17	Sharp Road - Florida Blvd	Rehab	09-AR-BD-0013	-	1,154	-	274,475	CSRS, Inc.	Reynolds, Inc.	\$17,492,855	1/15/2009	4/16/2010	7/7/2012
18	Brookstown Road - Evangeline Street (PH2)	Rehab	10-AR-BD-0040	-	1,075	-	84,000	CSRS, Inc.	John Plott Company	\$5,467,640	10/8/2009	11/12/2010	9/26/2012
19	Highland Road - Burbank Drive	Capacity	08-FM-ST-0023	-	-	39,400	-	GOTECH, Inc.	RACON, Inc.	\$20,591,067	3/31/2008	10/29/2010	11/12/2012
20	Brookstown Road - Evangeline Street (PH1)	Rehab	10-AR-BD-0039	-	1,150	-	161,000	CSRS, Inc.	Grady Crawford	\$10,309,180	7/10/2009	10/15/2010	11/13/2012
21	Group Project 1A (Veterans Parkway - Gravity Mains)	Capacity	08-GS-UF-0053	-	-	-	46,000	URS Corp.	Texas Sterling Const. Co.	\$19,581,108	3/10/2008	10/29/2010	1/4/2013
22	Choctaw Storage and PS Facility	WWTP	09-PS-UF-0009	3	-	25,000	-	CDM	Brasfield & Gorrie	\$43,237,000	4/14/2008	10/22/2010	1/9/2013
23	Zachary Area Transmission Network (PH4)	Capacity	10-FM-IF-0005	-	-	42,500	-	SJB/Owen & White	Wicker Construction	\$7,091,115	3/24/2008	8/27/2010	2/11/2013
24	SWWTP Wet Weather Improve (PH1)	WWTP	08-TP-BD-0033	-	-	-	-	CDM	Brasfield & Gorrie	\$108,443,892	6/23/2008	3/25/2010	4/18/2013
25	Zachary Area Transmission Network (PH3)	Capacity	10-FM-IF-0004	-	-	27,000	-	SJB/Owen & White	Hemphill Construction	\$8,947,920	3/24/2008	10/15/2010	6/6/2013
26	Zachary Area Transmission Network (PH1)	Capacity	10-FM-IF-0002	3	-	-	-	SJB/Owen & White	Max Foote Construction	\$18,486,500	3/24/2008	8/20/2010	7/10/2013
27	Staring Lane FM (PH2 - Highland to Perkins)	Capacity	06-WC-CP-0036	-	-	12,363	-	Monroe & Corie	JB James Construction	TBA	4/4/2008	8/6/2010	7/30/2013
28	Emergency Generators Installation	Other	09-PS-BD-0037	-	-	-	-	N/A	Grady Crawford	\$7,113,634	2010	-	2013
				17	7,316	449,908	1,353,415			\$411,590,620			

* All manholes are inspected in the project area. Only some are rehabilitated or replaced.

** Contractor is yet to be selected. The construction bid amount is the engineering estimate.

Project Information				Consultant Information	Cost	Schedule		
#	Project Name	Project Type	DPW Project #	Design Consultant	Estimated PDP Construction Value	Project Start	Advertise for Construction Bid	Project End
1	Bluebonnet Blvd - Jefferson Hwy Ph 1	Rehab	10-AR-MS-0043	CSRS, Inc.	\$6,685,000	2/8/2010	3/18/2011	7/10/2012
2	Multiple PS - Jefferson Highway - Park Forest Drive	Capacity	09-PS-MS-0046	CSRS, Inc.	\$2,620,000	6/8/2009	3/25/2011	10/18/2012
3	Perkins/Old Perkins Area - Booster PS514 Improvements	Capacity	09-PS-MS-0034	GEC	\$10,397,000	4/24/2009	4/8/2011	3/14/2013
4	Central Consolidation- PS42 FM	Capacity	09-FM-MS-0036	SJB/Owen & White	\$25,021,000	11/7/2008	4/15/2011	7/8/2013
5	Bluebonnet Blvd - Jefferson Hwy Ph 2	Rehab	10-AR-UF-0042	CSRS, Inc.	\$6,685,000	3/23/2010	4/15/2011	7/23/2012
6	Staring Lane FM (PH3 - Perkins to PS58)	Capacity	06-WC-CP-0036	Monroe & Corie	\$9,550,000	4/30/2009	4/29/2011	9/27/2013
7	Nicholson Dr - Highland Rd - Perkins Rd - PHB	Capacity	09-FM-MS-0047	Buchart - Horn	\$7,965,000	6/29/2009	5/20/2011	5/7/2013
8	Government St - S. Acadian Thruway	Capacity	09-GS-MS-0043	GSA Consulting Engineers, Inc.	\$4,680,000	8/28/2009	5/27/2011	11/8/2012
9	Acadian Thruway - Perkins Road	Rehab	10-AR-BD-0044	CSRS, Inc.	\$3,915,500	8/2/2010	5/27/2011	10/9/2012
10	Zachary Area Transmission Network Improvements - PH2	Capacity	10-FM-IF-0003	SJB/Owen & White	\$14,583,700	3/24/2008	6/24/2011	3/7/2013
11	Stanford Avenue - Morning Glory Road	Rehab	10-AR-BD-0045	CSRS, Inc.	\$6,876,000	8/2/2010	6/24/2011	10/26/2012
12	Central Consolidation FM (2,3,5,7,10)	Capacity	09-FM-MS-0033	Shread-Kuyrkendall & Associates, Inc.	\$10,601,000	11/7/2008	7/15/2011	8/19/2013
13	Bayou Duplantier Area Sewer Upgrades	Capacity	09-GS-MS-0042	Neel-Schaffer	\$4,374,000	8/31/2009	7/15/2011	6/27/2013
14	Central Consolidated Pump Stations (2,3,4,5,6,7,10 and 91)	Capacity	09-PS-MS-0035	Burk Kleinpeter / JIG	\$16,592,000	11/7/2008	7/29/2011	3/12/2013
15	Highland Road - Washington Street	Rehab	08-PI-UF-0051	CSRS, Inc.	\$8,022,000	10/11/2010	8/5/2011	12/14/2012
16	Group Project 1B (Veterans Parkway - PS and FM)	Capacity	08-PS-UF-0054	Evans-Graves / Burk Kleinpeter	\$19,309,000	3/10/2008	8/12/2011	1/24/2014
17	SWWTP Wet Weather Improve (PH2)	WWTP	08-TP-BD-0055	MWH	\$107,219,000	10/1/2008	8/19/2011	12/31/2014
18	Multiple PS - Nicholson Dr - Brightside Dr	Capacity	09-PS-MS-0048	Arcadis U.S., Inc.	\$6,113,000	9/14/2009	8/19/2011	1/31/2014
19	Acadian Thruway - Claycut Road	Rehab	10-AR-BD-0046	CSRS, Inc.	\$7,449,000	8/24/2010	8/19/2011	12/28/2012
20	Central Pump Station - PS 42	Capacity	09-PS-UF-0003	MWH	\$6,695,070	10/21/2008	8/26/2011	11/8/2013
21	PS 58 Overflow Pump Station	Capacity	09-PS-UF-0001	GEC	\$15,750,000	1/5/2009	9/9/2011	11/22/2013
22	O'Neal Lane Pipeline Projects A	Capacity	10-FM-MS-0008	URS Corp.	\$12,157,000	9/29/2009	9/9/2011	2/23/2013
23	O'Neal Lane Pipeline Projects B	Capacity	10-FM-MS-0008	URS Corp.	\$5,300,000	9/29/2009	9/9/2011	2/23/2013
24	Plank Road - Kleinpeter Road	Capacity	09-GS-UF-0028	Forte & Tablada	\$7,583,000	3/23/2009	10/28/2011	1/10/2014
25	Hooper Storage	WWTP	09-PS-UF-0007	TRC Engineers	\$19,115,000	1/19/2009	11/11/2011	12/24/2013
26	Airline Highway Pipeline Projects	Capacity	10-GS-MS-0007	ABMB Eng.	\$35,240,000	1/30/2009	1/13/2012	9/26/2014
27	Lovett Road - Greenwell Springs - A	Capacity	10-FM-MS-0049	SJB/Owen & White	\$11,364,000	5/3/2010	6/15/2012	11/29/2013
28	Lovett Road - Greenwell Springs - B	Capacity	10-FM-MS-0049	SJB/Owen & White	\$6,780,000	5/3/2010	6/15/2012	11/29/2013
29	Hooper Road Pump Station	Capacity	10-PS-MS-0048	Stanley	\$11,935,000	5/3/2010	7/6/2012	12/19/2014
30	O'Neal Lane Pump Station Projects A	Capacity	10-PS-MS-0050	MWH	\$12,226,000	5/25/2010	7/13/2012	12/26/2014
31	O'Neal Lane Pump Station Projects B	Capacity	10-PS-MS-0051	URS Corp.	\$9,800,000	5/25/2010	7/13/2012	12/16/2014
32	Multiple PS - Highland Rd - Kenilworth Parkway	Capacity	10-PS-MS-0009	AECOM	\$8,926,760	2/8/2010	10/5/2012	12/19/2014
33	Florida Blvd Pump Station Improvements	Capacity	11-PS-MS-0003	Brown & Caldwell	\$15,000,000	1/28/2011	10/26/2012	12/9/2014
34	Highland Road Pipeline Improvements A	Capacity	11-ES-PW-0002	Evans-Graves	\$9,741,000	1/28/2011	10/26/2012	4/11/2014
35	Highland Road Pipeline Improvements B	Capacity	11-ES-PW-0002	Evans-Graves	\$8,118,000	1/28/2011	10/26/2012	4/11/2014
36	Sherwood Forest Blvd - Goodwood Blvd Pipeline Improvements	Capacity	11-FM-MS-0005	Forte & Tablada	\$10,200,000	1/28/2011	4/5/2013	9/9/2014

UNDER DESIGN

484,588,030

Projects to be Advertised for Construction

The following projects are expected to advertise for construction bids in April 2011:

- Perkins/Old Perkins Area - Booster PS514 Capacity Improvement Project
- Central Consolidation – PS42FM (Phase A)
- Bluebonnet Blvd – Jefferson Highway Phase 2
- Staring Lane FM Phase III – Perkins to PS58

Projects to be Advertised for Engineering Selection

Pump Road Pump Station Capacity Improvement Project.

Estimated Construction Cost - \$9,300,000. This project consists of replacing five and upgrading three pump stations. Expected to advertise for RFQ in May 2011.

Multiple PS – Burbank Drive – Siegen Lane Capacity Improvement Project.

Estimated Construction Cost - \$4,100,000. The project includes replacement of six pump stations. The new pump stations will work in conjunction with forcemain upgrades in other South Forced Lower Basin projects to alleviate chronic SSOs at and near these pump stations. Expected to advertise for RFQ in May 2011.

Oak Villa Blvd – Monterey Blvd Capacity Improvement Project.

Estimated Construction Cost - \$9,000,000. This project includes the upsizing of the gravity sewer upstream of PS16, PS50, and PS51 and the forcemain from PS16, which is being upgraded as part of the Multiple PS – Florida Blvd. – Sherwood Forest Blvd. project. Expected to advertise for RFQ in May 2011.

Joor Road – Greenwell Springs Capacity Improvement Project.

Estimated Construction Cost - \$6,900,000. This project involves the design and construction of forcemain upgrades in the North Forced West Basin. The upgrades are designed to alleviate chronic SSOs at the pump stations and increase the forcemain capacity. The upgrades range in size from 6 to 24 inch diameter. Expected to advertise for RFQ in May 2011.

Baton Rouge SSO program progress report

march 2011

300 North Boulevard, Room 208
Baton Rouge, LA 70802
(225) 389-3158
DPW@brgov.com

